

Overall Spatial Structure and Near-term Delivery

Use the rail heritage corridor as the framework, define three key districts and prioritise mobility continuity, service gaps and retrofit



NEAR-TERM TASKS: CONNECT ROUTES, FILL SERVICE GAPS, RETROFIT SPACE, ASSIGN OWNERS

Start with a 1 km pilot and three nodes while verifying boundaries, tenure, rail safety, utilities and operating funds.



0-3M: BASE DATA + INITIATION

4-12M: PILOT DELIVERY

13-24M: DISTRICT ROLL-OUT

PROGRAM REGISTER

11.41 km²

overall working base

3

key delivery districts

6

near-term projects

0—24月

proposed delivery window

NEAR-TERM CONTROLS

- 01 verify formal boundaries and tenure
- 02 review rail safety and utilities first
- 03 coordinate public and revenue uses
- 04 assign delivery, operations and maintenance

Key Delivery Districts and Near-term Projects

Coordinate announced scale, working base, first projects, delivery conditions and responsibilities



EXISTING-SPACE RETROFIT

Ground-floor access, barrier-free routes, stormwater and staffed service are delivered as one project.

KEY-DISTRICT PROJECT REGISTER

P-03 Zhongzhiyuan Validation District

192.1 ha / 192.9 ha

1.5 ha controlled validation field

tenure · fire/traffic · ethics/data

P-04 AI Origin Collaborative District

104.3 ha / 104.3 ha

3,000 m² shared ground floor

tenure · structure/fire · operations

P-02 Dazhongsi Station-City District

72.0 ha / 72.0 ha

station-city public-hall interface

flow/evacuation · rail · fire

Published and recalculated areas differ by less than 0.5%; official extents remain subject to statutory confirmation.


Project Review Requirements for Public AI Services

Review accountable owner, human service, data use, stop authority, complaints and annual evaluation for twelve proposed services



Functional Zoning, Area Balance and Renewal Method

Six renewal-unit types record area balance, retrofit, new uses, facility additions and delivery conditions

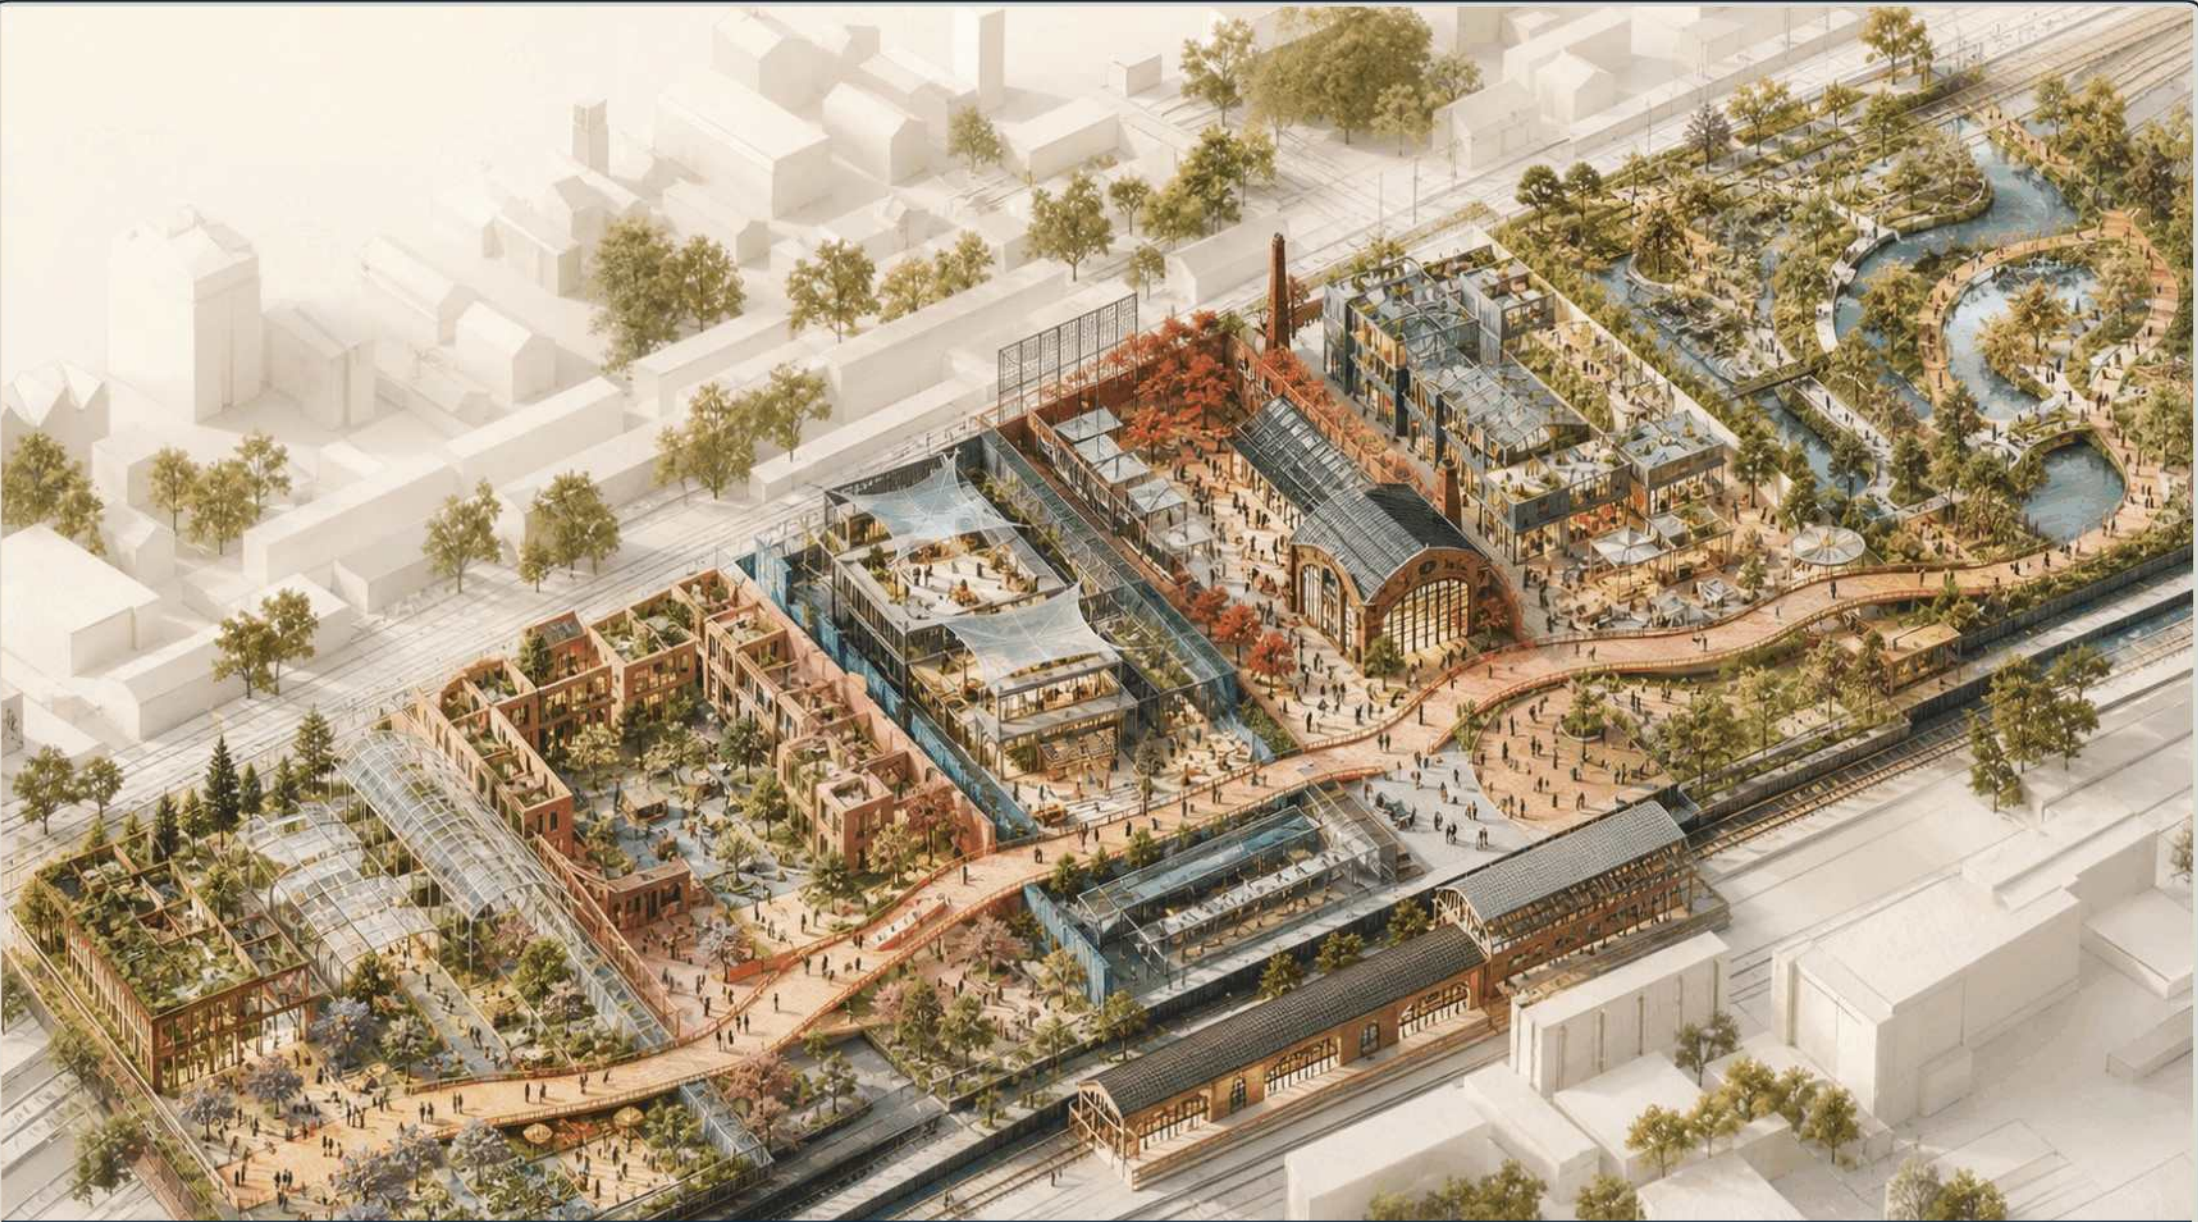

SIX RENEWAL UNITS WITH DEFINED TASKS AND DELIVERY CONDITIONS

The zones support project coordination; statutory use, intensity and compatibility are confirmed through implementation planning.

LAND + TASK REGISTER

LU-01 R&D + safety review

208.6 ha · 18.3%

LU-02 talent housing + amenities

214.4 ha · 18.8%

LU-03 training + technology transfer

204.9 ha · 17.9%

LU-04 rail culture + public service

180.8 ha · 15.8%

LU-05 digital service + commerce

166.2 ha · 14.6%

LU-06 blue-green + utilities


166.4 ha · 14.6%

1141.3 ha

working-base zone total

Near-term Mobility and Stormwater Delivery Requirements

Address mobility gaps, limited rest and fragmented drainage through coordinated walking, cycling, shade, stormwater and service stops

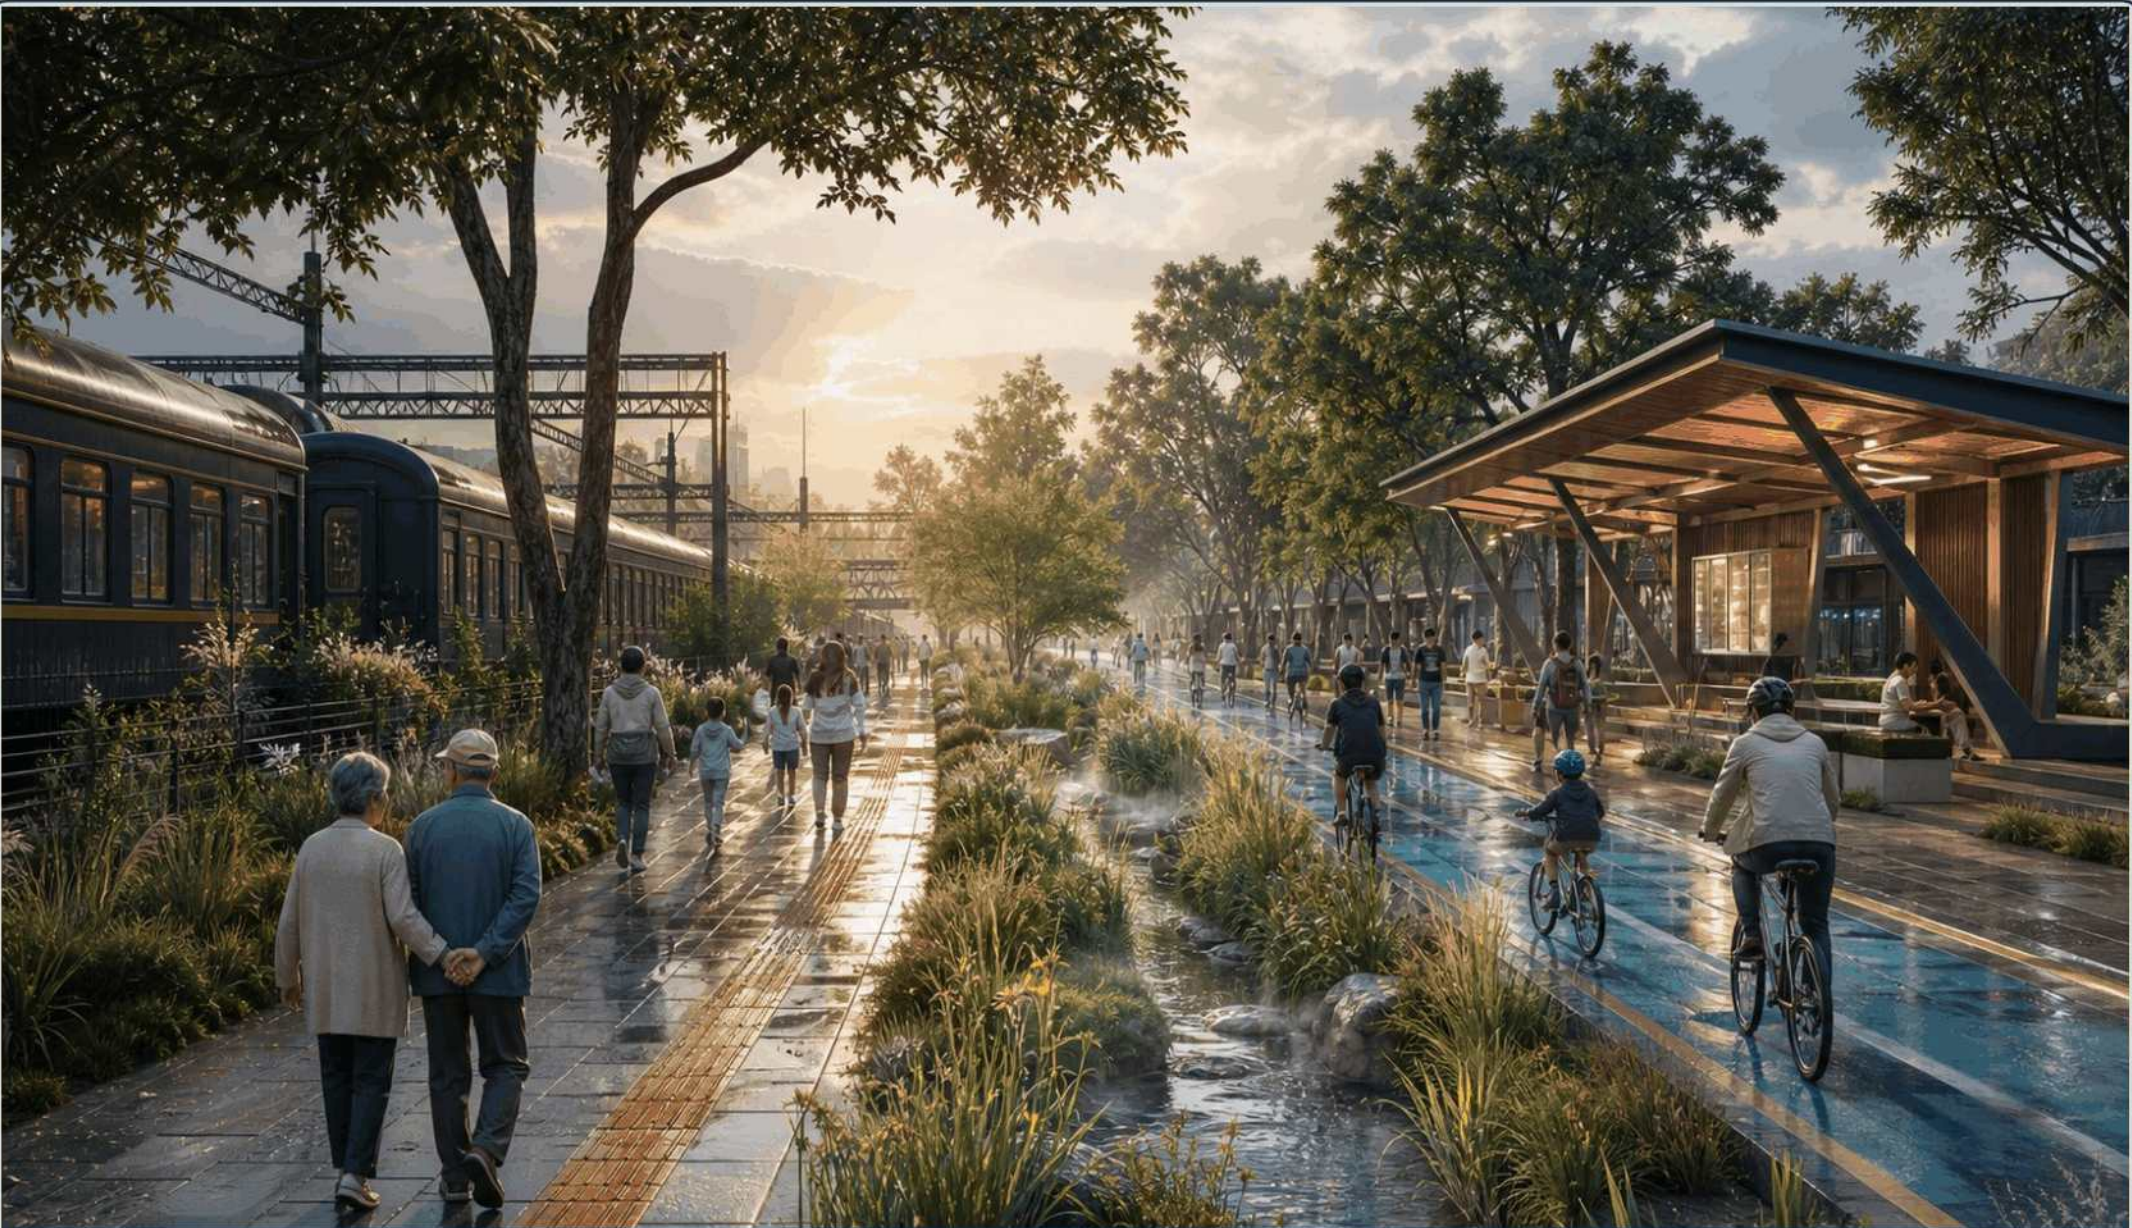

ILLUSTRATIVE COMPLETED VIEW OF THE MOBILITY PILOT

Walking, cycling, stormwater and service stops are coordinated within a 12 m typical section.

CLIMATE + SPATIAL RESPONSE

35.58°C daily Tmax P95

22.3 d/y days ≥35°C

649.1 mm annual rain

4.05 daily solar

12 m FLEXIBLE EDGE




walk rain cycle service

3.0 m 2.5 m 4.0 m 2.5 m

clear width · drainage · shade + rest

Planning Indicator Management and Acceptance

Nine indicators are assigned to base-map checks, design control and operating assessment with methods, owners and review cycles

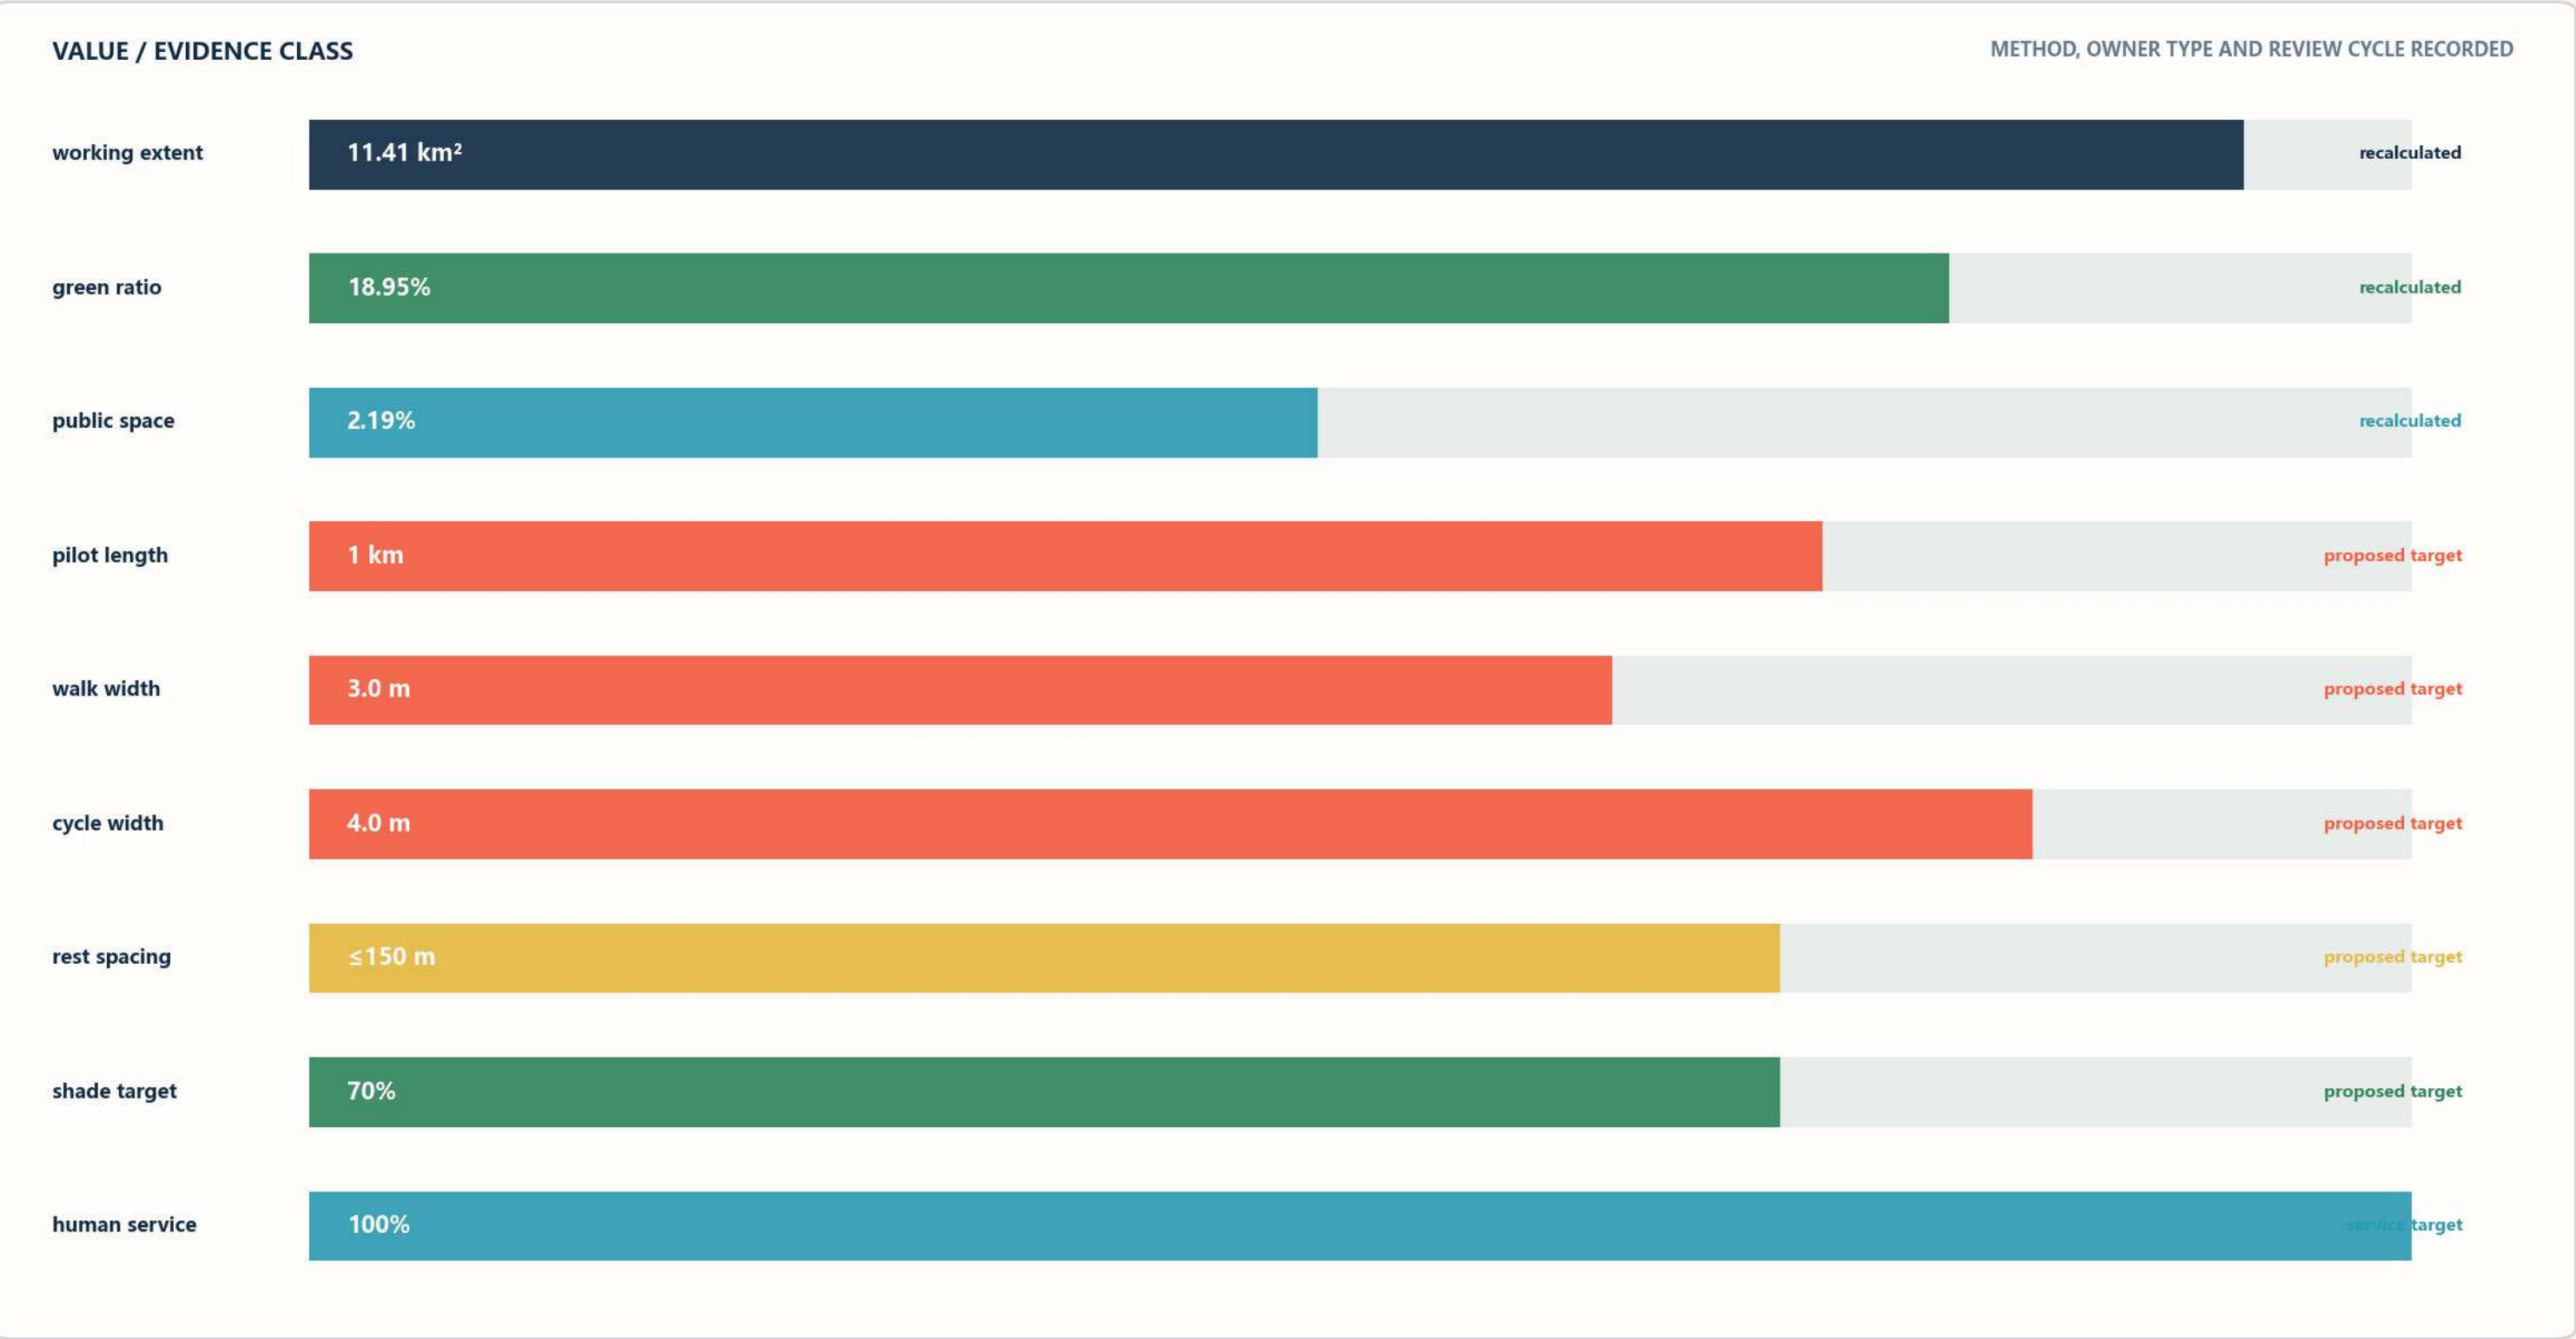

Priority-user Needs and Project Rectification List

Review mobility, stay, human service and construction impacts for nine priority user groups
REGISTERED USER ISSUES 0-3

Children and families	3		2		3		
Older people and caregivers	1	3	3				1
Disabled users	3		1		1	2	
Long-term residents			1		3		1
Renters and small businesses	1		1	3	3		1
Students and young talent			3	3		1	
Commuters and visitors	3				1		
Frontline service and maintenance staff			1	2		1	3
Nearby campuses, parks and public institutions				1	2	1	
	mobility	rest + care	human service	learning + work	delivery burden	data + digital	maintenance + takeover

SURVEY + ACTION ARRANGEMENT

09

priority-user registers

09

targeted walk-throughs

00

current coverage findings

Coverage is calculated after population, employment and time-of-day flow baselines; current action follows group issue lists.

Near-term Project Register and Delivery Conditions

Six near-term projects record scope, prerequisites, cost class, schedule, acceptance and operator type

SIX NEAR-TERM PROJECT CARDS

SCOPE | OWNER TYPE | WINDOW | PREREQUISITES | OUTPUT

P-01

Jingzhang mobility pilot

SCOPE 1 km walking, cycling, stormwater and rest

OWNERS district · subdistrict · rightsholder

WINDOW 6-18 months | M

START 3 prerequisites

P-02

Dazhongsi station connection

SCOPE four-way access, wayfinding, service and parking

OWNERS subdistrict · station · transport · rightsholder

WINDOW 12-24 months | L

START 3 prerequisites

P-03

Zhongzhiyuan R&D test field

SCOPE 1.5 ha R&D test, safety buffer and training

OWNERS park · test bodies · safety evaluator

WINDOW 12-24 months | L

START 4 prerequisites

P-04

AI Origin shared ground floor

SCOPE 3,000 m² learning, talent and shared work

OWNERS rightsholder · subdistrict · campus/community · operator

WINDOW 9-18 months | M

START 3 prerequisites

P-05

public-service node prototype

SCOPE 320 m² staffed service, amenities and stormwater

OWNERS subdistrict · community · facility operator

WINDOW 6-12 months | M

START 4 prerequisites

P-06

public-AI management system

SCOPE applications, joint review, work orders and evaluation

OWNERS district · service operators · evaluator

WINDOW 3-9 months | S

START 4 prerequisites

FUNDING + OPERATIONS

01

PUBLIC SPACE + AMENITIES

capital plan names asset recipient and maintenance body

02

REVENUE + SHARED SPACE

rightsholder and operator cost retrofit, lease and staff

03

R&D TEST + DIGITAL SERVICE

implementer funds equipment, insurance, safety and upkeep

04

PRE-START FUNDING GATE

capital, annual O&M and staffing documented together

COST CLASS: S <5m | M 5–20m | L 20–50m CNY

Typical-section Controls for the Jingzhang Pilot

A 12-m typical section addresses walking gaps, mixed traffic, limited rest and stormwater drainage



PILOT DELIVERY VIEW | accessible walk + rain garden + two-way cycling + human service

SECTION CONTROLS + ACCEPTANCE

12.0 m total | four continuous functional bands

01 WALKING ≥3.0 m

continuous clear width, tactile and kerb-ramp links

ACCEPT field width survey

02 STORMWATER ≥2.5 m

complete inflow, overflow and drainage route

ACCEPT hydraulic check + flow test

03 CYCLING ≥4.0 m

two-way operation with speed control at crossings

ACCEPT marking width + conflict review

04 SERVICE EDGE ≥2.5 m

seating, shade and staffed wayfinding

ACCEPT facility list + access audit

DELIVERY INTERFACES

- coordinate rail protection and maintenance access
- integrate street limits, utilities and existing trees
- retain physical wayfinding and human service during outages

Public-service Node Delivery and Operations Guide

A 320 m² prototype defines site, program, staffing, utilities, acceptance and exit requirements



NODE AXONOMETRIC INTENT | 20 m × 16 m | continuous accessible loop

NODE DELIVERY + OPERATIONS

250–400 m² program range | 320 m² prototype

01 FOOTPRINT 320 m²

20 m × 16 m prototype with demountable components

ACCEPT site and built-area check

02 HUMAN SERVICE 24–36 m²

counter, waiting, storage and staffed position

ACCEPT hours and staffing roster

03 MICROCLIMATE ≥70%

continuous shade across principal stay areas

ACCEPT summer solar study + field audit

04 RESPONSE 60 s / 24 h

human acknowledgement and routine fault logging

ACCEPT monthly response + work-order log

HANDOVER + EXIT MANAGEMENT

- joint utilities, fire, access and site-permit review
- facility list, duty register and monthly inspection record
- remove equipment if operations lapse; retain basic civic amenities

Regional Coordination Tasks and Delivery Responsibilities

Define lead types, supporting bodies, annual tasks and filed outputs for testing, talent, transfer, station services and blue-green operations



ANNUAL COORDINATION TASKS

Each task records lead type, prerequisites and filed outputs

RC-01 AI safety evaluation

LEAD TYPES park operator · university lab · evaluator

OUTPUT versioned report and failure cases

RC-02 campus-community learning

LEAD TYPES university · community · operator

OUTPUT course edition and review record

RC-03 technology transfer

LEAD TYPES technology service · park operator · rightsholder

OUTPUT referral register and rights statement

RC-04 station-city public service

LEAD TYPES station operator · subdistrict · transport

OUTPUT task test and site-inspection record

RC-05 blue-green operations

LEAD TYPES landscape · municipal · local operator

OUTPUT as-built file, inspection and work orders

DELIVERY MECHANISM



Delivery and Operating Management for Public AI Services

Define accountable bodies, tasks and filed outputs across initiation, review, testing, opening and evaluation

12

PROPOSED SERVICES

8


REVIEW CONDITIONS

60 s

HUMAN ACKNOWLEDGEMENT

5 days

PUBLIC RESPONSE

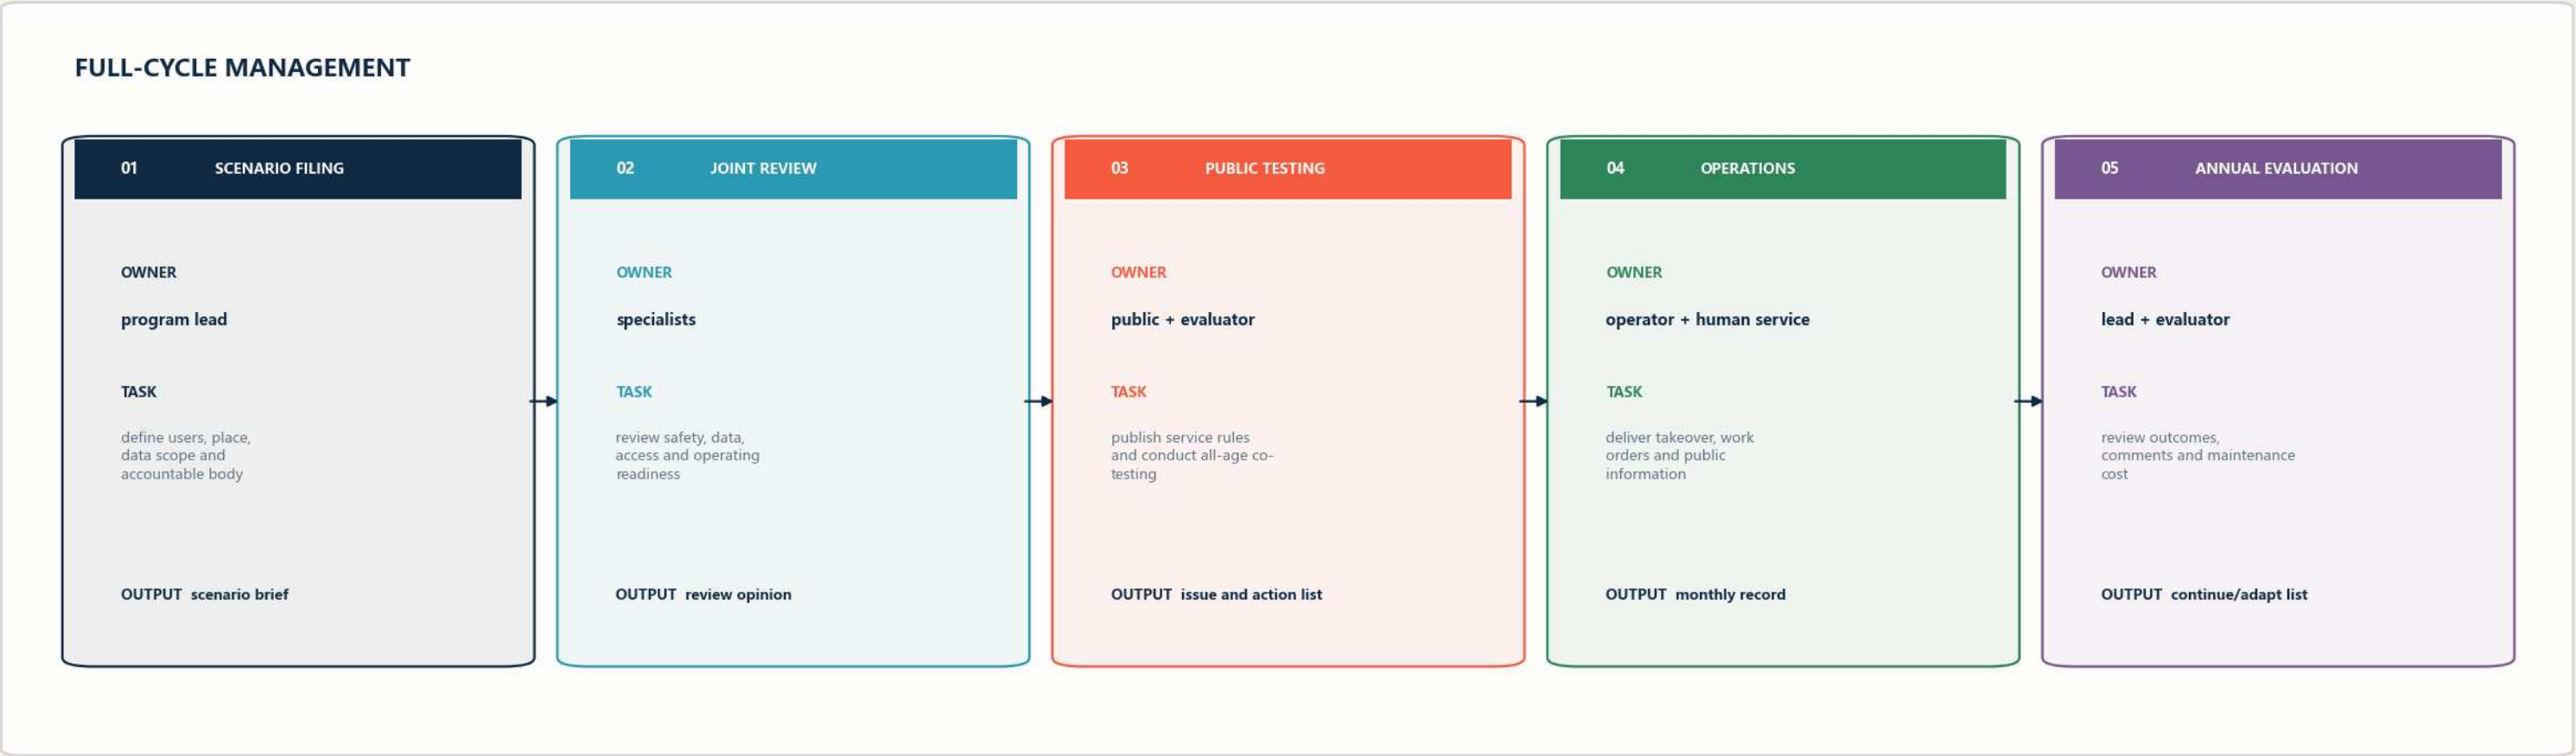

SERVICE ACCESS

Maintain human/non-digital access and physical wayfinding during outages

DATA MANAGEMENT

Collect data required by purpose; publish use, retention and complaint route

SAFE OPERATIONS

Isolate critical faults and switch to human service; log routine faults within 24h

PUBLIC OVERSIGHT

Monthly fault summary, quarterly rule review and annual adjustment list

Phased Delivery Plan and Annual Evaluation

Six actions proceed through early start, pilot delivery, corridor works and annual evaluation
PROPOSED 0-24 MONTH DELIVERY WINDOW



Planning Basis and Material-use Statement

Materials are classified, sourced, managed by use and reviewed as an updatable planning record

8

MATERIAL CLASSES

30

PLANNING FIGURES

4

PDF DELIVERABLES

2

LANGUAGE SETS

MATERIAL	SOURCE / RIGHT	PLANNING USE	MANAGEMENT REQUIREMENT	STATUS
proposal text and translations	agent-authored for this submission	original submission text	policy and standard summaries remain attributed	REGISTERED
technical figures and diagrams	generated locally from submission data by the package build script	agent-authored graphics	provisional geometry is labelled and cannot be treated as statutory mapping	REPRODUCIBLE
OpenStreetMap context	OpenStreetMap contributors	ODbL 1.0 attribution	background context only; no ownership or statutory inference	LICENSED
NASA POWER climate baseline	NASA POWER daily API documentation and retrieved values	public scientific data with attribution	concept-stage point-grid baseline; engineering design requires local data	REGISTERED
Blender corridor rendering	agent-generated from conceptual massing	agent-authored rendering	not an as-built or surveyed model	CONCEPT
generated concept scenes	OpenAI image generation directed for this submission	submission concept imagery	design intent only; no identifiable real people or official endorsement	ILLUSTRATIVE
Three.js offline viewer	Three.js 0.185.1 bundled locally	MIT license	license notice retained in source package	LICENSED
system fonts	Microsoft YaHei or available CJK system font	render-only local font use	font files are not redistributed	EMBEDDED

STATUTORY BASIS

Policies, standards and task sources are indexed in the source register

TECHNICAL BASE

The working base is updated with official boundaries, survey and current-condition records

DELIVERABLE USE

Concept visuals convey planning intent; delivery proceeds through specialist design outputs

Public-space Identity and Wayfinding Guidelines

A three-level system coordinates corridor gateways, direction signs and service confirmation



HIERARCHY + APPLICATION

A continuous, legible and all-age public-information system

L1 | CORRIDOR GATEWAY

At district entrances and station-city interfaces; show identity and overall direction

L2 | DIRECTION SIGN

At route decisions; show destination, distance, accessible route and interchange

L3 | SERVICE CONFIRMATION

At service nodes; show hours, human desk, status and feedback route

INFORMATION + MAINTENANCE

- Separate project identity from government emblems and maintain a clear information boundary
- Every AI service point includes a human-service sign and non-digital access instructions
- Coral marks duty, service status and stop information; navy and cyan support routine navigation
- Inspect monthly, create and publish a routine-fault work order within 24 hours

